



Service Package: Healthcare Solution Gap Analysis (6 weeks)

A structured, phase-by-phase framework for identifying, prioritizing, and closing architectural gaps in your existing healthcare solution — delivering interoperability, compliance, and future readiness.

TOGAF ADM

6-WEEK SPRINT

HEALTHCARE IT

Week 1: Foundation & Baseline Architecture

Objective: Establish a shared understanding of the current state, define the project scope, and align all key stakeholders on goals, constraints, and expectations before any architectural analysis begins.

Core Activities

- Conduct a formal kick-off meeting with all relevant stakeholders — clinical, technical, compliance, and executive — to align on the scope, timeline, and success criteria of the gap analysis.
- Review all existing documentation, including applications and application components, data repositories, Health Information Exchange (HIE) integrations, system interfaces, and past architecture decisions.
- Identify and register key stakeholders along with their specific concerns, influence levels, and communication preferences.
- Begin systematic documentation of the Baseline Architecture, capturing the current-state systems, data flows, integration points, and technology stack in line with TOGAF ADM Phase A & B entry criteria.

Key Deliverables

Stakeholder Register

A comprehensive registry of all individuals and groups with a vested interest in the architecture, including roles, concerns, and influence levels. This serves as the foundation for all future communication and workshop planning.

Initial Baseline Architecture Document

A structured description of the current-state healthcare solution — encompassing business processes, data models, application landscape, and underlying technology infrastructure. Forms the "as-is" anchor for all subsequent gap analysis work.

Week 2: Target Architecture Definition

Objective: Define the desired future state of the healthcare solution by capturing business requirements, strategic drivers, and regulatory imperatives. This target becomes the benchmark against which all gaps are measured.

Core Activities

- Facilitate structured workshops with business and technology stakeholders to elicit and document formal business requirements, strategic drivers (e.g., value-based care, patient engagement), and non-functional requirements such as scalability and security.
- Develop the Target Architecture Vision, with a specific focus on healthcare interoperability standards (HL7 FHIR, IHE profiles), data management modernization, and full compliance with HIPAA, GDPR, and applicable state regulations.
- Identify and catalogue the key Architecture Building Blocks (ABBs) that constitute the Target Architecture — including API gateways, clinical data repositories, identity management systems, and analytics platforms.

Key Deliverables

Architecture Vision Document


A high-level narrative and visual representation of the proposed future-state architecture. This document captures the strategic rationale, stakeholder concerns to be addressed, and the overall direction of the transformation initiative. It serves as the north star for all remaining phases.

Draft Target Architecture ABBs

A structured catalogue of Architecture Building Blocks that define the reusable components, services, and patterns required to achieve the target state. Each ABB is described with its function, interfaces, and compliance considerations, enabling consistent architectural decision-making throughout the engagement.

Week 3: Qap Identification — Business & Data Domains

Objective: Conduct a rigorous side-by-side comparison of the baseline and target architectures within the Business and Data domains to surface all material discrepancies, shortfalls, and transformation requirements.

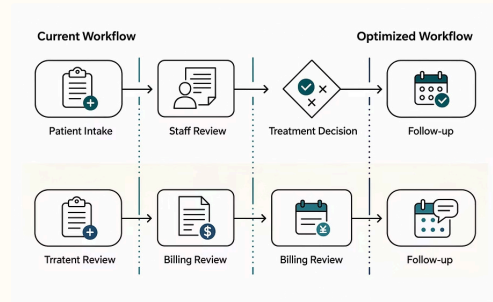


Business Architecture Analysis (Phase B)

Systematically compare current and target business architectures across all dimensions: organizational structures, business capabilities, healthcare workflows, care pathways, and governance models. Identify where current processes fall short of supporting strategic objectives such as care coordination, patient-centered delivery, and value-based reimbursement models. Document each gap with a business impact assessment and ownership assignment.

Deliverable: Business Architecture Qap Analysis Report

A detailed report documenting all identified gaps in business capabilities, processes, and organizational structures, with impact ratings, root cause notes, and recommended disposition for each gap item.

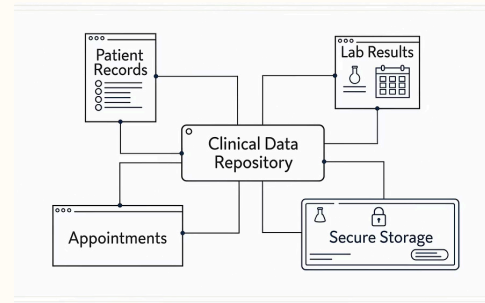

Data Architecture Qap Analysis


Analyze the current data landscape against target requirements across four critical dimensions: data **currency** (timeliness and freshness), data **location** (where data resides and how it is accessed), data **availability** (uptime and accessibility), and data **relationships** (referential integrity, master data management, and semantic interoperability). Gaps are documented with associated regulatory risk where applicable.

Deliverable: Data Architecture Qap Analysis Report

A comprehensive data gap register covering data quality, integration, governance, and lifecycle management deficiencies — mapped to regulatory requirements including HIPAA minimum necessary standards and GDPR data minimization principles.

Week 4: Gap Identification — Applications & Technology Domains

Objective: Extend the gap analysis into the Application and Technology layers, identifying shortfalls in the software portfolio, integration architecture, infrastructure, and operational tooling that prevent achievement of the target state.

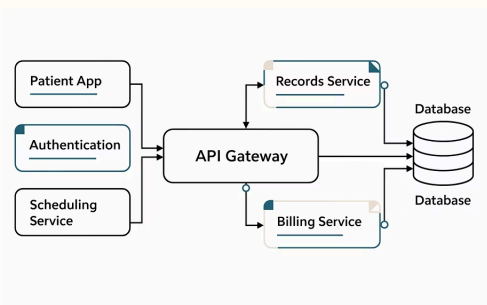

Application Architecture Analysis (Phase C)

Compare the current application portfolio against the Target Architecture's application blueprint. Evaluate clinical applications (EHR, CPOE, CDSS), patient engagement platforms, care management tools, and integration middleware against target capabilities. Identify redundant applications, capability voids, integration gaps (e.g., missing FHIR-compliant APIs), and lifecycle risks (e.g., end-of-life systems). Assess the current application rationalization posture and alignment with the interoperability target.

 Deliverable: Application Architecture Qap Analysis Report

A structured gap register for the application layer, including capability mapping, integration gap identification, application rationalization recommendations, and alignment scores against target ABBs.

A structured gap register for the application layer, including capability mapping, integration gap identification, application rationalization recommendations, and alignment scores against target ABBs.



Technology Architecture Analysis (Phase D)

Assess the underlying technology infrastructure — including on-premise servers, cloud platforms, network architecture, security infrastructure, and DevOps tooling — against the Target Architecture requirements. Identify gaps in platform currency, cloud readiness, disaster recovery posture, cybersecurity controls (particularly relevant given HIPAA Security Rule requirements), and observability capabilities. Document infrastructure debt and vendor support risks.

 Deliverable: Technology Architecture Gap Analysis Report

A comprehensive assessment of infrastructure and platform gaps, including security posture findings, cloud migration readiness indicators, infrastructure debt quantification, and technology lifecycle risk ratings.

A comprehensive assessment of infrastructure and platform gaps, including security posture findings, cloud migration readiness indicators, infrastructure debt quantification, and technology lifecycle risk ratings.

Week 5: Gap Analysis Synthesis & Prioritization

Objective: Consolidate findings from all four architectural domains into a unified, actionable gap register. Apply a structured prioritization methodology to ensure the most impactful gaps are addressed first in the roadmap.

Core Activities

- Aggregate all gap findings from the Business, Data, Application, and Technology domain reports into a single, deduplicated Comprehensive Gap Analysis Report with cross-domain linkages identified.
- Apply a multi-criteria prioritization model scoring each gap across: **business impact** (effect on patient outcomes, revenue, and strategic objectives), **regulatory risk** (HIPAA/GDPR compliance exposure), **feasibility** (effort, cost, and technical complexity), and **stakeholder urgency**.
- Identify and classify candidate Architecture Roadmap components — grouping related gaps into logical work packages or transformation initiatives that can be sequenced and resourced.
- Validate prioritization results with key stakeholders to ensure business alignment before roadmap development commences.

Prioritization Framework

Critical Gaps

High business impact + high regulatory risk. Must be addressed in the first roadmap phase. Examples: HIPAA security control deficiencies, broken interoperability interfaces.

High Priority

Significant capability shortfalls with moderate effort. Targeted for second roadmap phase. Examples: legacy application replacements, data quality remediation.

Strategic Opportunities

Longer-term enhancements that enable future capabilities. Scheduled in later roadmap phases. Examples: analytics platforms, AI/ML enablement.

Key Deliverables

- **Comprehensive Gap Analysis Report** — consolidated master gap register across all four TOGAF domains.
- **Prioritized Gap List** — scored and ranked gaps with disposition recommendations and proposed roadmap phase assignments.

Week 6: Roadmap Development & Finalization

Objective: Translate prioritized gap findings into a structured, executable Architecture Roadmap. Refine and finalize all project deliverables, and secure stakeholder approval to move into implementation planning.

Core Activities

- Develop the Architecture Roadmap (TOGAF ADM Phase E — Opportunities & Solutions) outlining phased work packages, each with defined scope, dependencies, resource estimates, and success criteria to close prioritized gaps.
- Define transition architectures where necessary — interim states that enable incremental delivery while maintaining operational continuity for critical clinical systems.
- Conduct a formal quality review of all deliverables produced during the engagement — ensuring consistency, completeness, and alignment with the Architecture Vision established in Week 2.
- Prepare and deliver the Final Stakeholder Presentation, covering key findings, gap priorities, roadmap phases, and recommended next steps. Facilitate a structured review and approval session.

Key Deliverables



Architecture Roadmap

A phased, time-bound plan of work packages that systematically address all prioritized gaps. Each phase is scoped with objectives, dependencies, milestones, and resource requirements — aligned with organizational capacity and strategic priorities. Includes transition architecture definitions where applicable.



Final Presentation Deck

A comprehensive executive-ready presentation summarizing the entire 6-week engagement: methodology, stakeholder findings, gap analysis results across all four domains, prioritization rationale, and the Architecture Roadmap. Structured for both executive approval and operational hand-off.

Key TOGAF Deliverables

The following deliverables are produced throughout the 6-week engagement in alignment with TOGAF ADM phases. Each artifact serves a distinct purpose and contributes to the overall architectural knowledge base for the organization.



Stakeholder Register

Identifies all individuals, teams, and organizational groups with an interest in or influence over the architecture. Captures roles, concerns, influence levels, and preferred communication channels. Used throughout the engagement to ensure no critical perspectives are missed and to guide workshop facilitation and stakeholder communications.



Architecture Vision Document

A high-level strategic overview of the proposed architecture transformation — created early in the engagement to align stakeholders before detailed analysis begins. Articulates the key drivers, constraints, and intended outcomes of the architecture change initiative, ensuring executive sponsorship and organizational alignment throughout the project.



Architecture Roadmap

A structured, phased plan for implementing the target architecture and systematically closing all prioritized gaps. Organized into logical work packages with defined scope, sequencing, dependencies, and resource estimates. Includes transition architecture definitions to support incremental delivery while maintaining operational continuity for critical patient-facing clinical systems.



Baseline Architecture Document

A structured, evidence-based description of the current state of the healthcare solution across all four TOGAF domains — Business, Data, Application, and Technology. Serves as the authoritative "as-is" reference throughout the gap analysis, ensuring all discrepancies are measured against a documented and validated starting point.



Architecture Building Blocks (ABBs)

Reusable, vendor-neutral architectural components that define the capabilities and services required in the target state. In the healthcare context, ABBs may include FHIR-compliant API gateways, clinical data repositories, identity and access management services, consent management platforms, and real-time analytics engines. ABBs provide a consistent design language across the architecture.



Target Architecture Document

Outlines the desired future state of the healthcare solution in full architectural detail. Defines the capabilities, data structures, application portfolio, and technology infrastructure required to meet business objectives, support interoperability standards, and achieve regulatory compliance. Serves as the "to-be" benchmark for all gap calculations.



Gap Analysis Report

The central artifact of the engagement — a comprehensive, cross-domain register of all identified discrepancies between baseline and target architectures. Each gap entry includes a description, affected domain, business impact rating, regulatory risk assessment, root cause notes, and recommended disposition. Serves as the direct input to roadmap development and prioritization activities.

Qantt Chart: 6-Week Engagement Timeline

The following illustrative Gantt chart maps all key activities across the 30-day engagement. Activities are organized by week and work stream, providing a clear picture of sequencing, dependencies, and parallel workstreams across the TOGAF ADM phases.

Activity / Deliverable	Week 1	Week 2	Week 3	Week 4	Week 5	Week 6
Kick-off & Scope Definition	●● Days 1–2					
Stakeholder Register	●●● Days 1–3					
Baseline Architecture Documentation	●●● Days 3–5					
Target Architecture Workshops		●●● Days 6–8				
Architecture Vision Document		●● Days 8–9				
Target Architecture ABBs Definition		●● Days 9–10				
Business Architecture Gap Analysis			●●● Days 11–13			
Data Architecture Gap Analysis			●● Days 13–15			
Application Architecture Gap Analysis				●●● Days 16–18		
Technology Architecture Gap Analysis				●● Days 18–20		
Gap Synthesis & Prioritization					●●● Days 21–23	
Roadmap Component Identification					● Day 24–25	
Architecture Roadmap Development						●●● Days 25–27
Final Deliverable Review & QA						● Day 28
Stakeholder Presentation & Approval						●● Days 29–30



Note: The Gantt chart above is illustrative. Actual task durations, dependencies, and ownership assignments should be refined during the Week 1 kick-off session based on team size, organizational complexity, and availability of existing documentation. Parallel workstreams in Weeks 3 and 4 assume at least two dedicated architects working concurrently on domain-specific gap analysis activities.

Conclusion: Bridging the Gap for a Future-Ready Healthcare Solution

The 6-week TOGAF-driven gap analysis framework provides a rigorous, proven methodology for understanding exactly where your healthcare solution stands today — and precisely what must change to achieve a future-ready, interoperable, and compliant target state.

Structured TOGAF Rigor

By grounding the analysis in the TOGAF Architecture Development Method (ADM), the engagement ensures comprehensive coverage across all four architectural domains — Business, Data, Application, and Technology — with no critical dimension overlooked. The standardized deliverable set creates lasting organizational assets that extend well beyond the 6-week engagement.

Interoperability & Data Integrity

The structured identification of integration and data gaps provides a clear, evidence-based path toward achieving true healthcare interoperability — enabling seamless data exchange between EHRs, HIEs, payers, and patient-facing applications — while simultaneously strengthening data governance, quality, and lineage across the enterprise.

Compliance & Risk Reduction

By explicitly mapping gaps to HIPAA, GDPR, and applicable regulatory frameworks throughout the analysis, the engagement produces a prioritized list of compliance remediations that directly reduces organizational risk exposure — protecting both patient data and the institution from regulatory penalty and reputational harm.

Actionable Roadmap

The engagement concludes not with a list of problems, but with a prioritized, phased Architecture Roadmap — giving the organization a clear, sequenced plan for closing gaps, allocating resources efficiently, and measuring progress. The result is a robust, future-proof healthcare solution fully aligned with organizational strategy and patient care goals.

A well-executed TOGAF gap analysis does not just identify what is missing — it illuminates the precise path from where you are to where you need to be, with every step grounded in stakeholder alignment, architectural evidence, and strategic intent.
